CONSTRUCTION SCHEDULE

Valley Baptist Church

Project Start: 9/15/2019

TASK DESCRIPTION	START	END	TYPE
Phase 1 Construction	9/15/2019	1/26/2020	
Secure Building Permit	9/15/2019	9/17/2019	B
Start Sitework & Excavation	9/18/2019	10/8/2019	G
Form Footings & Place Concrete	9/29/2019	11/16/2019	R
Form Concrete Walls & Insulate	10/13/2019	11/2/2019	Y
Place Concrete in Wall Forms	11/5/2019	11/10/2019	O
New Garage	10/27/2019	12/8/2019	P
Grade New Parking & Gravel	10/27/2019	11/6/2019	X
Steel Erection	11/10/2019	12/22/2019	B
Winterize Site	12/22/2019	12/26/2019	G
BFC Winter Meeting	1/24/2020	1/26/2020	R
Phase 2 BFC Construction	3/31/2020	11/8/2020	
Underground Utilities	3/31/2020	4/21/2020	B
Plumbing Rough-In	3/31/2020	4/17/2020	G
Slab on Grade	4/17/2020	4/20/2020	R
First Floor Toping Slab	4/20/2020	4/23/2020	Y
Lumber Delivery	4/23/2020	5/1/2020	O
Truss Delivery	5/1/2020	5/3/2020	P
Set Up Tents	5/1/2020	5/7/2020	X
BFC Tool Trailer Arrives	5/7/2020	5/9/2020	B
BFC Saw Team Arrives	5/13/2020	5/13/2020	G
Frame and Erect Walls for Roof Trusses	5/17/2020	5/23/2020	R
Install Welded Door Frames	5/17/2020	5/23/2020	Y
Rough-In Electrical in Walls	5/17/2020	6/6/2020	O
Install Roof Trusses & Decking	5/24/2020	5/30/2020	P
Complete Framing of Interior Walls	5/24/2020	5/30/2020	X
Complete All Framing	5/31/2020	6/6/2020	B

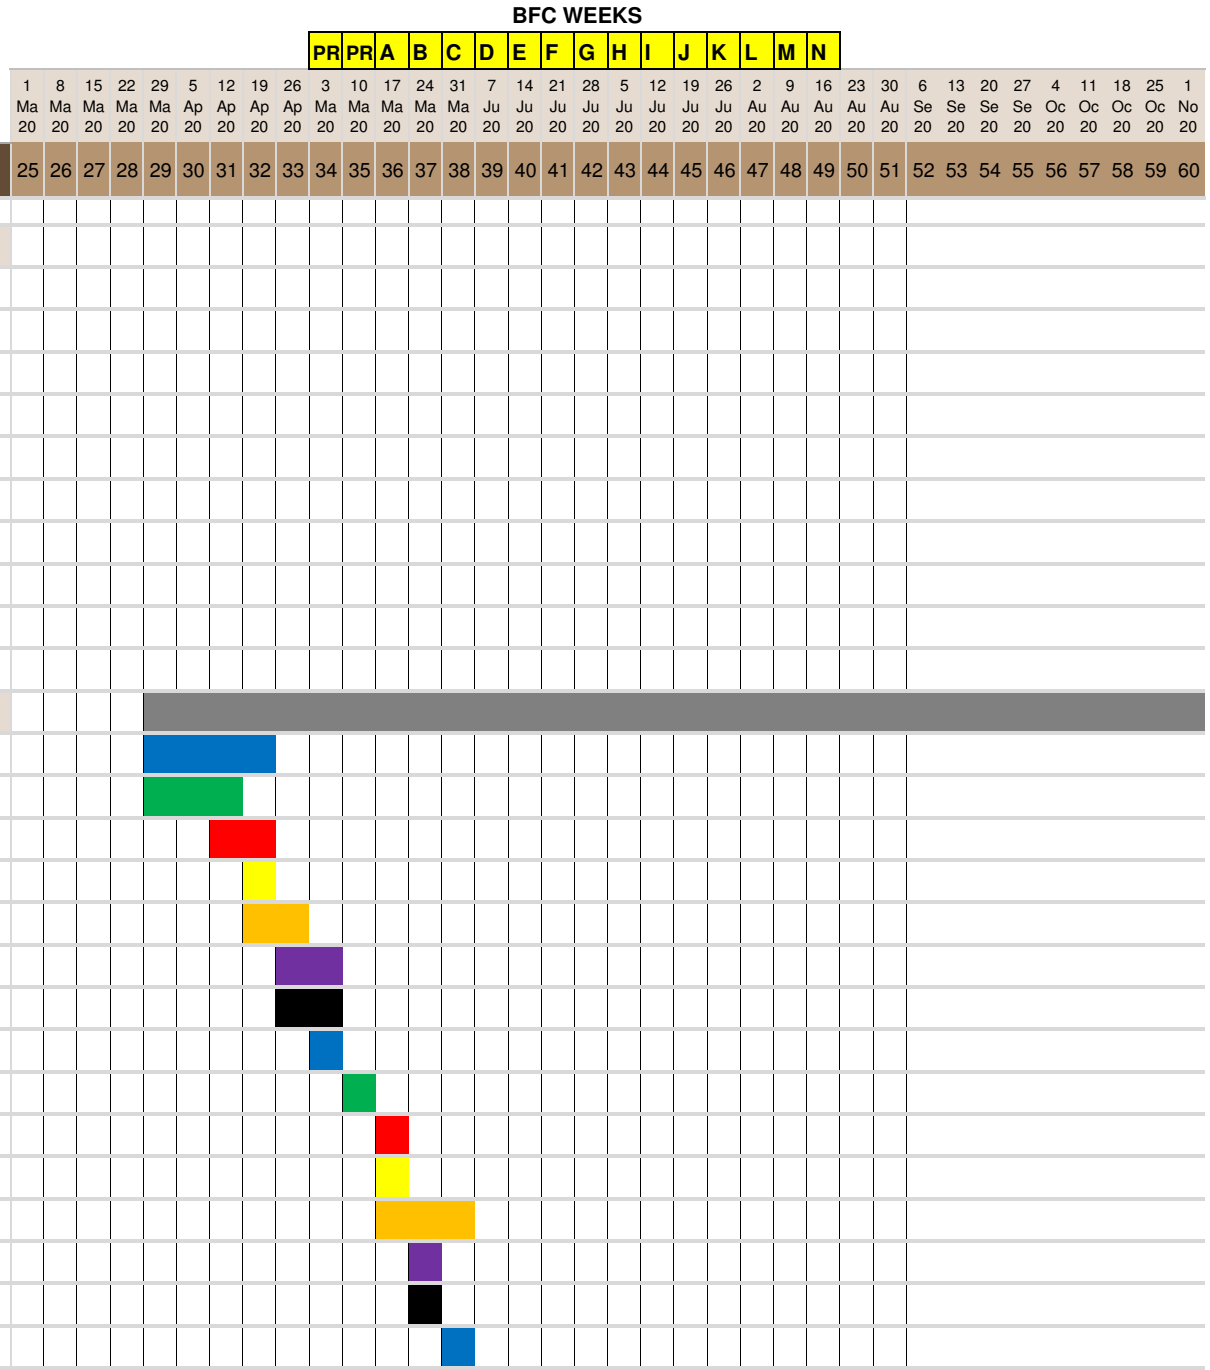

CONSTRUCTION SCHEDULE

Valley Baptist Church

Project Start: 9/15/2019

TASK DESCRIPTION	START	END	TYPE
Install Insulation at Mech. Room	5/31/2020	6/6/2020	G
Install Drywall at Mechanical Room	5/31/2020	6/6/2020	R
Dry-In all Segments of Building	5/31/2020	6/6/2020	Y
Install Facia	5/31/2020	6/6/2020	O
Begin Fire Protection (Subcontract)	5/31/2020	8/15/2020	X
Install Roof Felt & Ice and Water Shield	5/31/2020	6/6/2020	P
Install Air Handlers in Mech. Rooms	6/7/2020	6/13/2020	X
Install HVAC Ductwork & Small VAV boxes	6/7/2020	6/20/2020	B
Install Roofing	6/14/2020	6/20/2020	G
Install Wall Insulation	6/14/2020	6/20/2020	R
Install Small Windows Downstairs	6/14/2020	6/20/2020	Y
Install Masonry Wainscot	6/14/2020	7/4/2020	O
Wire Branch Circuits	6/14/2020	6/20/2020	P
Install Attic & Roof Insulation	6/21/2020	6/27/2020	X
Secure Rough-In Inspections (Mech&Elec)	6/14/2020	6/20/2020	B
Install Drywall	6/28/2020	7/11/2020	G
Install Exterior WoodSoffit Framing	6/28/2020	7/11/2020	R
Install Exterior Siding, Soffit & Eve Trim	7/5/2020	7/11/2020	Y
Tape and Finish Drywall	7/5/2020	7/26/2020	O
Caulk Exterior	7/5/2020	7/11/2020	P
Paint Exterior Trim	7/5/2020	7/11/2020	X
Paint Walls of Rooms w/Acoustical C	7/12/2020	7/18/2020	B
Install Acoustical Ceiling Grid	7/19/2020	7/25/2020	G
Install Interior Trim	7/19/2020	8/2/2020	R
Install HM KD Door Frames	7/9/2020	7/19/2020	Y
Install HVAC Duct Runouts	7/19/2020	7/25/2020	O
Install Light Fixtures in Acoustical Ceilings	7/19/2020	7/29/2020	P

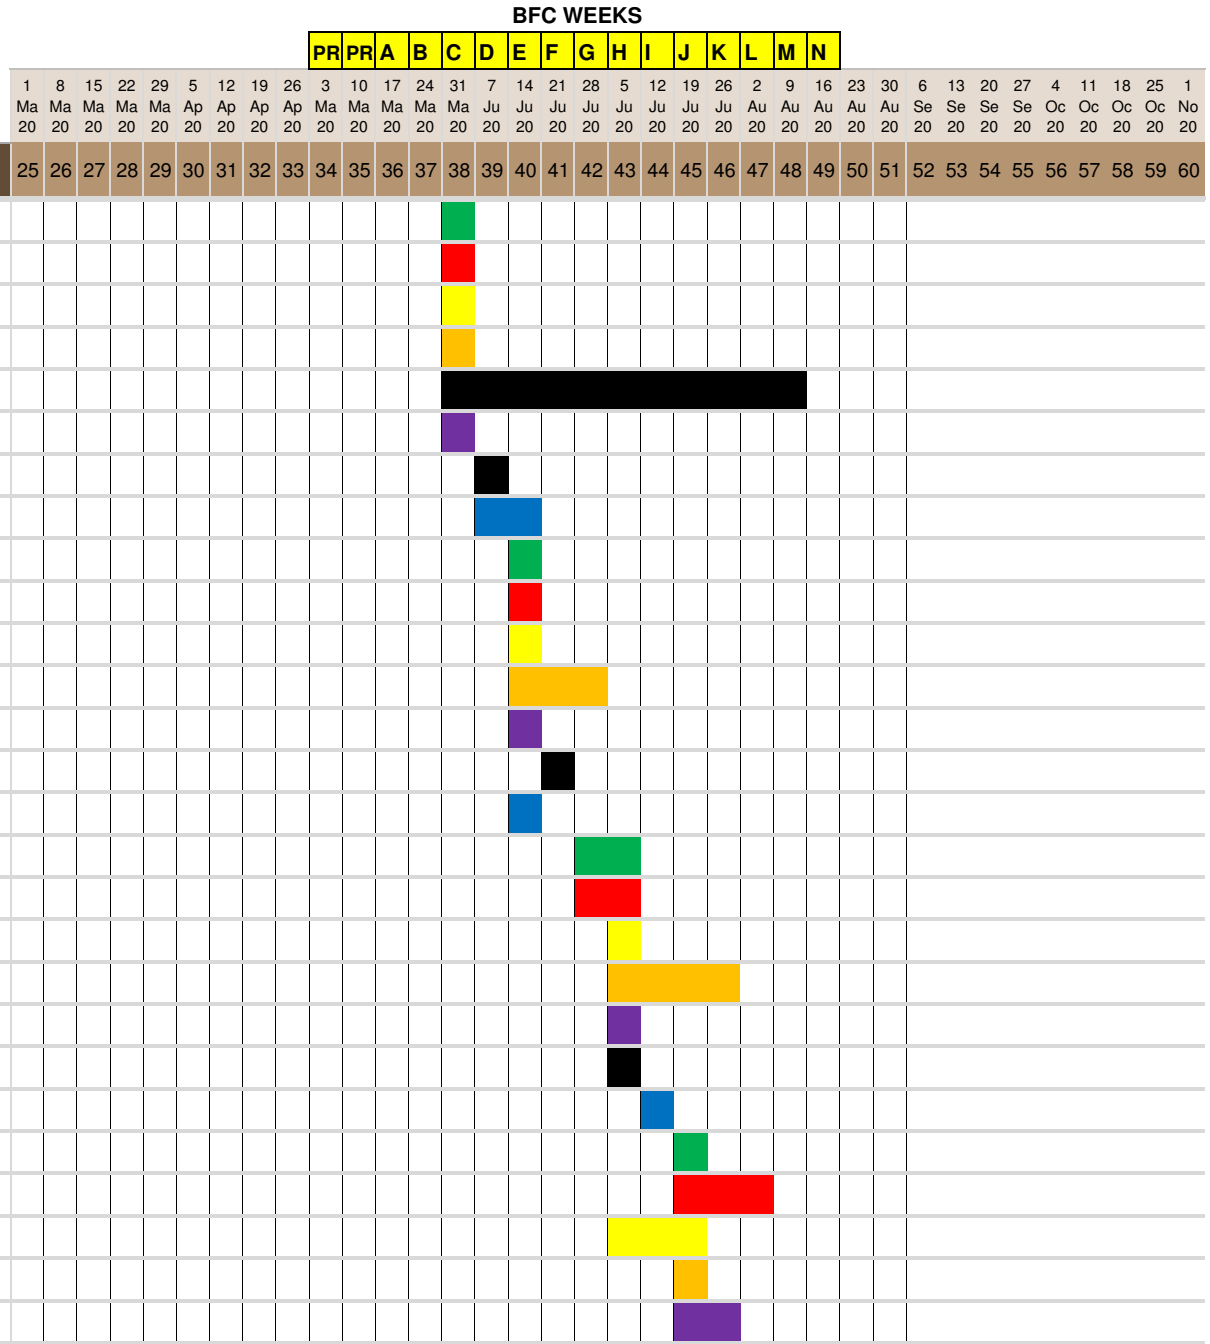

CONSTRUCTION SCHEDULE

Valley Baptist Church

Project Start: 9/15/2019
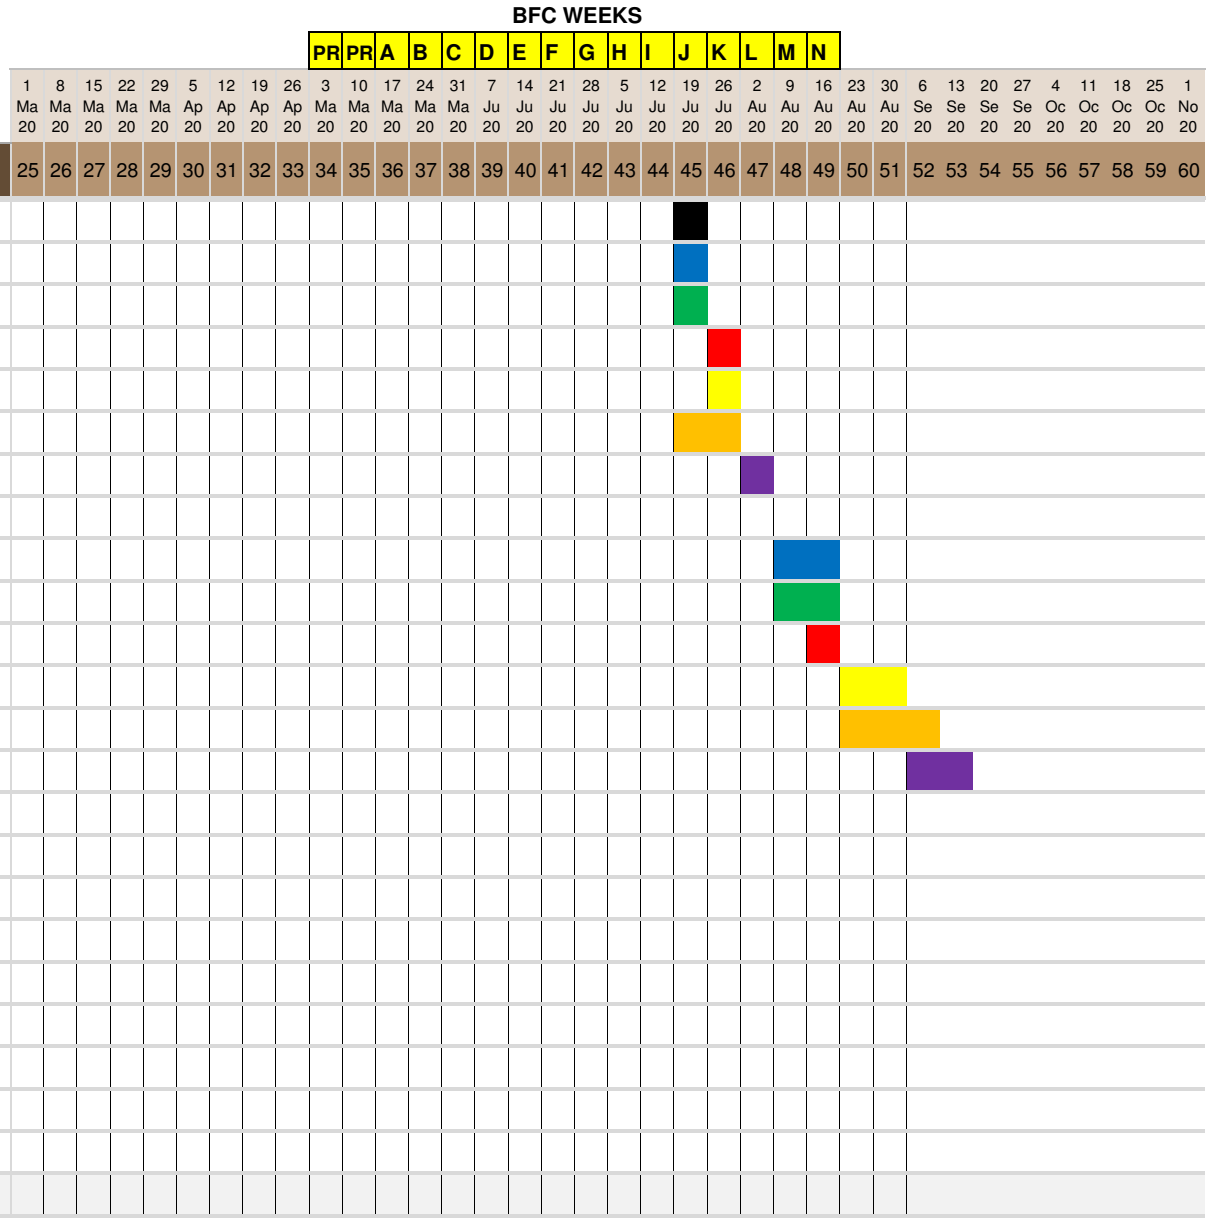
TASK DESCRIPTION	START	END	TYPE
Paint Interior Walls at Cabinet Locations	7/19/2020	7/25/2020	X
Paint Drywall Ceilings	7/19/2020	7/25/2020	B
Permanent Power for Building	7/25/2020	7/25/2020	G
Startup HVAC Systems	7/26/2020	7/28/2020	R
Install Acoustical Celling Tile	7/28/2020	7/31/2020	Y
Paint Remaining Drywall & HM Frames	7/25/2020	7/31/2020	O
Install Hard Tile	8/2/2020	8/8/2020	P
Install Millwork	08/09/20202	8/16/2020	X
Install Toilet Partitions	8/9/2020	8/16/2020	B
Mass Painting	8/9/2020	8/16/2020	G
Install Vinyl Flooring	8/16/2020	8/22/2020	R
Install Soft Flooring	8/23/2020	9/1/2020	Y
Install Landscaping	8/23/2020	9/7/2020	O
Install Asphalt Paving	9/7/2020	9/17/2020	P
Stripe Parking Lot	9/22/2020	9/22/2020	X
Install Landscaping	9/17/2020	10/1/2020	B
Complete Punch List	10/1/2020	10/15/2020	G
Final Inspections	10/15/2020	10/20/2020	R
Certificate Of Occupancy	10/23/2020	10/25/2020	Y
BFC Trailers Depart	10/23/2020	11/8/2020	O
Install Furniture	10/25/2020	10/29/2020	P
Soft Opening	11/1/2020	11/8/2020	X
Dedication Sunday	TDB	X	X
